

Conventional Facilities and Construction Schedule

Nobuhiro Terunuma
KEK

ATF2 Project Meeting, 2007/12/19, KEK

Floor base structure



Finalize the floor




Shield Installation


Used shields from FFAG (KEK)
Can not move them anymore,
without the cleanup of ATF2.



Final Shield Layout

-  Installed/stored
-  will be delivered from Feb/4 to Mar/14.


About 70% of side wall was installed at present.
A few blocks will be delivered every day after Feb. 4th.

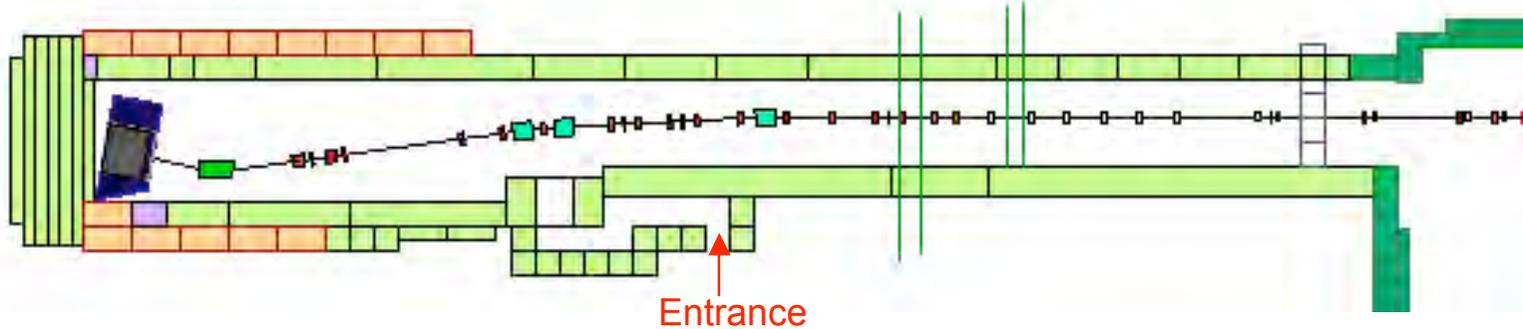

Beam line will be closed by shields until end of March 2008.
Open any shield when install the remaining magnets; FD, Bend,...




Plan of Huts for devices

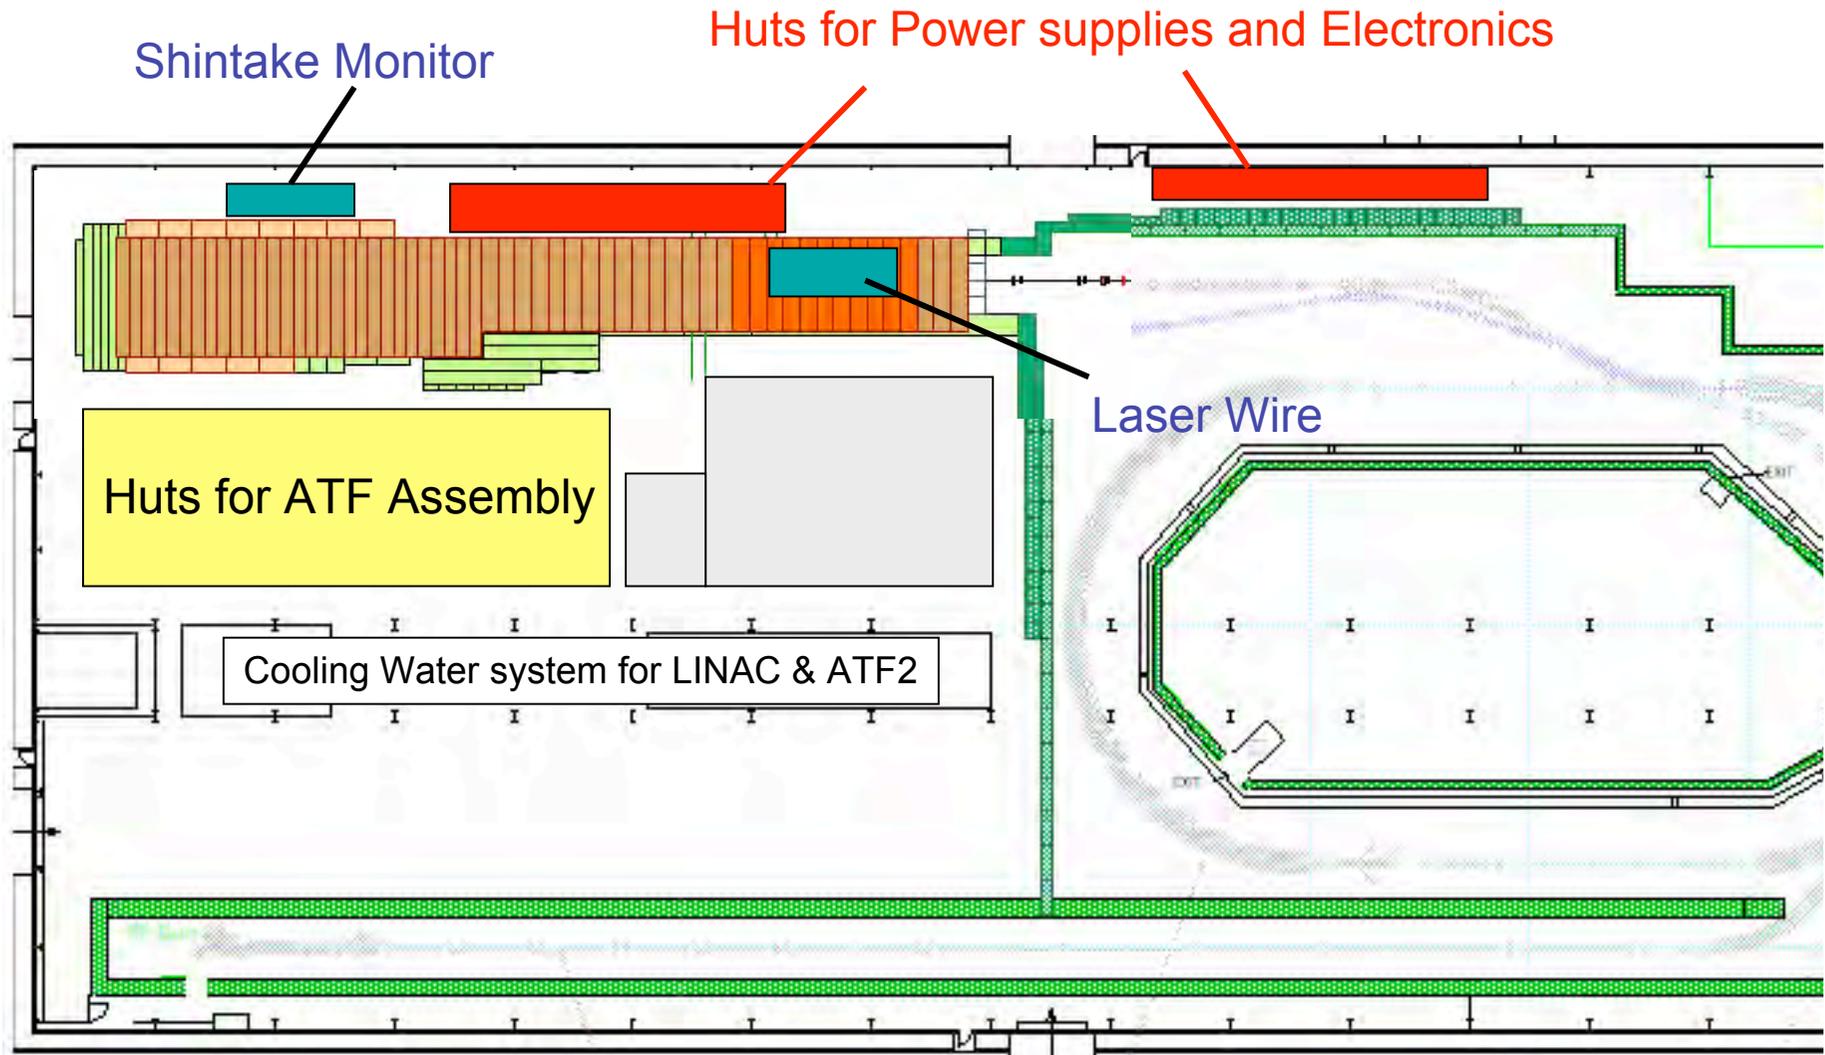


ATF2 Construction Schedule

Not changed since Dec. 2006.

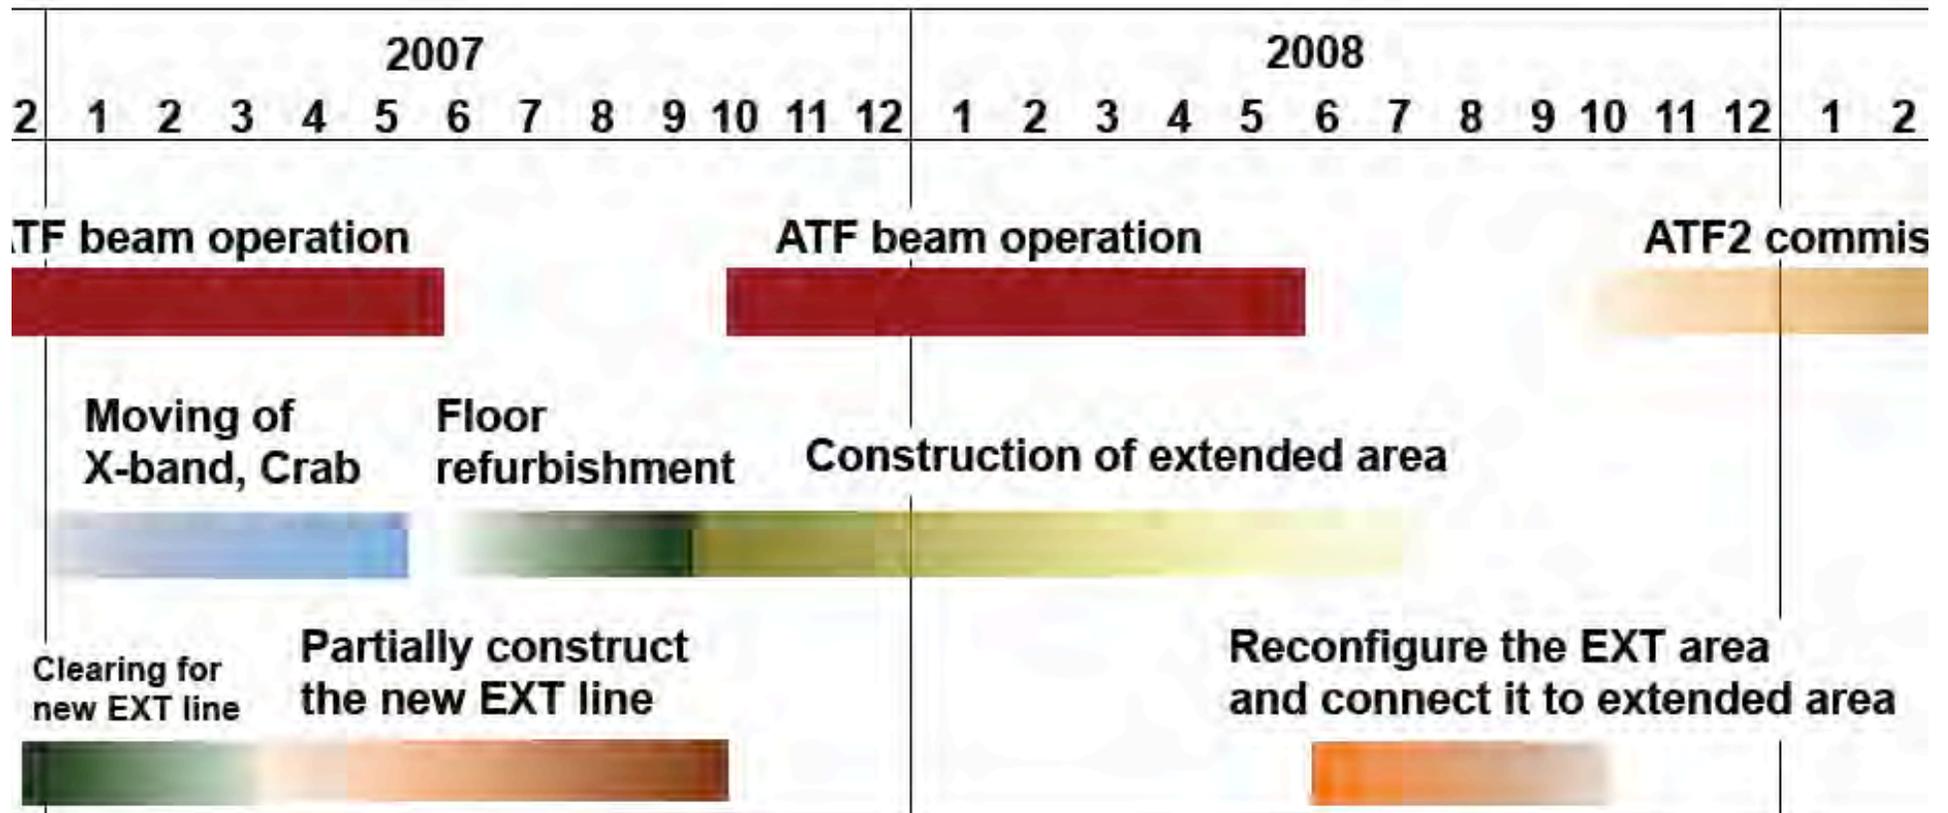

Construction schedule until June for ATF2 area

ATF2 area

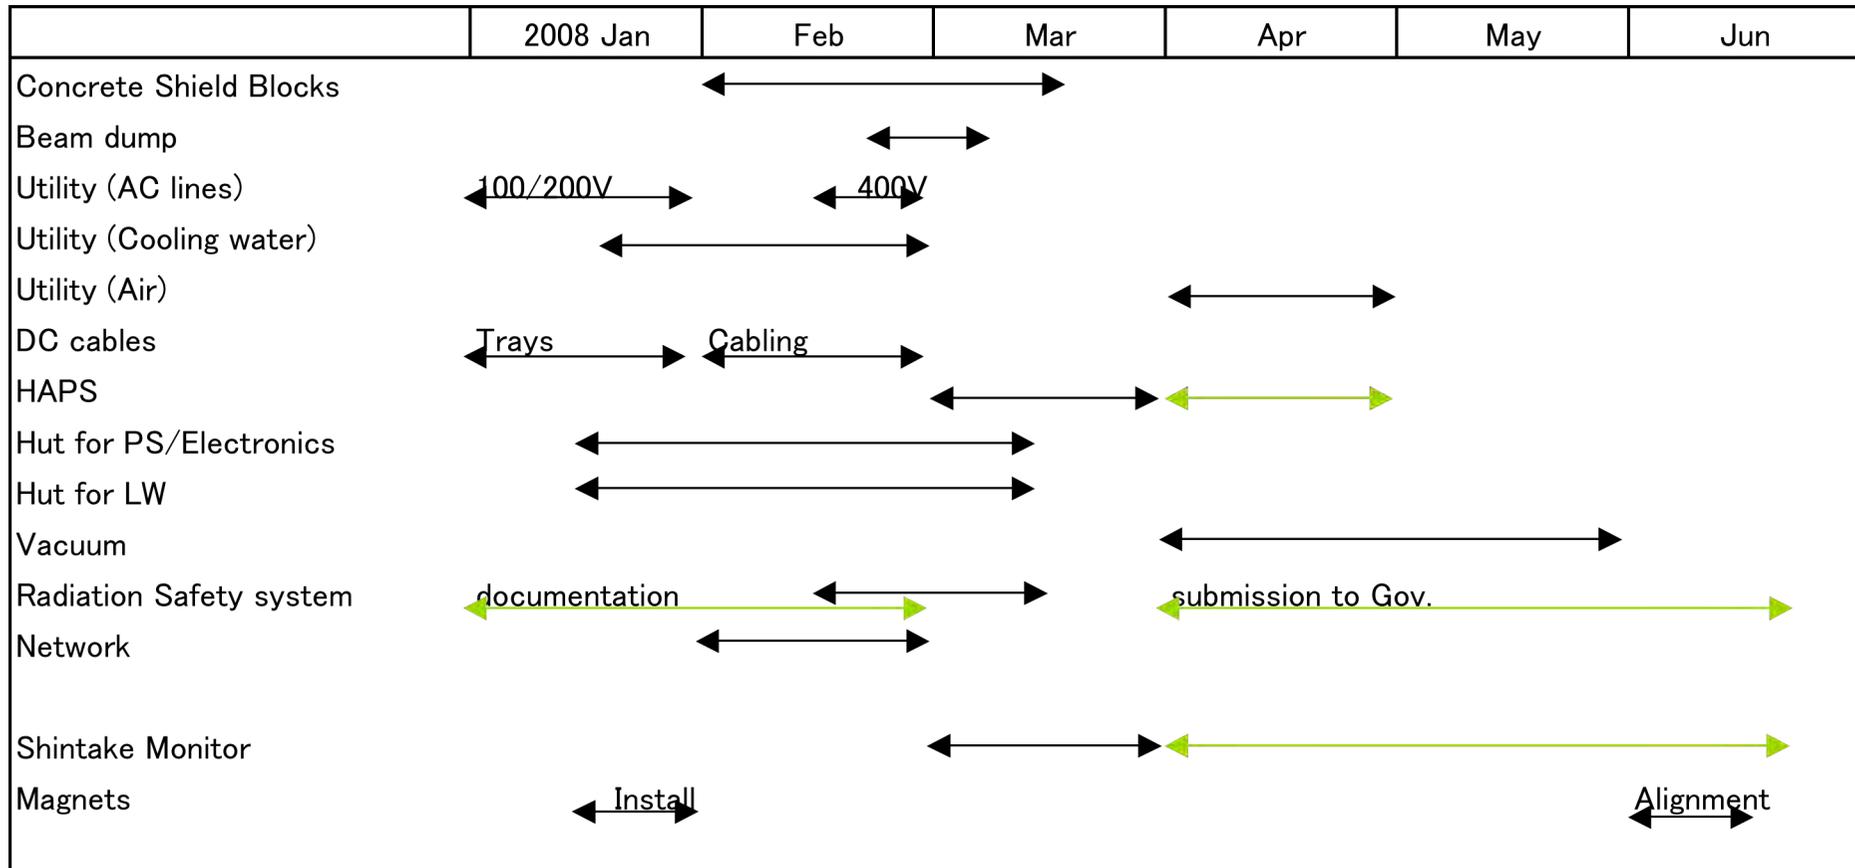

Construction schedule

EXT-ATF2 area

