


Cryomodule (S1-G)

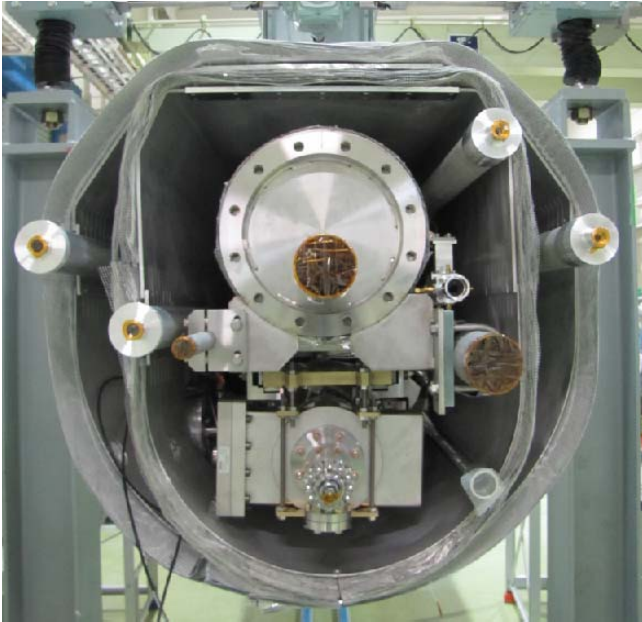

S1-G Module-C assembly

- Feb. 8-12
 - Tuner and magnetic shield assembly by INFN and FNAL.
- Feb. 15~Mar. 10
 - Alignment of four cavities.
 - Attaching temperature sensors and pin diode.
 - Assembling 5K shield, and mounting SI on the 5K shield.
 - Connecting thermal intercepts.
 - Assembling 80K shield, and mounting SI on the 80K shield.
- Mar. 11-12
 - Inserting the cold mass into the vacuum vessel.
 - The module-C will be moved into the STF tunnel.

S1-G Module-A assembly will begin in April.

- Mar. 8
 - KEK four cavity string went out from the clean room.



2010/3/10

Memorial Photo
(8th, Mar. 2010')



Photo by Toge-san

ILC-ML-Webex
